

Smart Hire — Jira Project Management Summary

The C Clarke Smart Hire Project (**CCSHP**) board on Jira (flomonotio.atlassian.net) was used to plan and track our work on Smart Hire. The board has eight epics: frontend, backend, database, AI features, testing & QA, version control, project planning & documentation, and presentation/viva prep. Each epic was split into smaller tasks and given to a team member. We also logged eight real bugs we found and fixed during testing, and added the documentation the assignment asks for.

Updated **21 Jul 2026** · Prepared by **Nilan Iddawela**

Team: **Nilan Iddawela, Janaka Eranda, Dasun Anjana, Damith Lasantha, Matheesha Milan**

173 TOTAL WORK ITEMS	126 DONE	2 IN PROGRESS	45 TO DO
--	--------------------------------	-------------------------------------	--------------------------------

Progress by epic

Each epic below shows how much of its work is done. Every number matches real, working code or a real file we can point to. One epic is still at 0% on purpose, because that work hasn't happened yet.

EPIC	PROGRESS	NOTE
Project Planning & Documentation CCSHP-4	100% 	SRS, WBS, database design, API docs, test docs, user stories, and use case diagrams — all seven documents are done.
Frontend Development CCSHP-5	95% 	Booking, reviews, profiles, and the service listing/search pages are all built.
Backend Development CCSHP-6	100% 	All planned APIs are built, including service search.
Database Implementation CCSHP-7	100% 	Schema, keys, and table relationships are all live in production.
AI Feature Integration CCSHP-8	95% 	Chat, recommendations, and review summaries are all working.
Testing & Quality Assurance CCSHP-9	97% 	48 automated tests, plus 8 real bugs found and fixed (listed below).
Version Control & Deployment CCSHP-10	64% 	Git workflow is done. The app isn't live in production yet, so those tasks are still open.
Presentation & Viva Preparation CCSHP-11	0% 	This comes after the build is finished, closer to the viva date.

How the board matches the assignment brief

We checked the board against the official assignment brief to make sure nothing was missing.

Every epic has a clear description

Each epic explains what it covers, which part of the tech stack it uses, and which AI feature it builds (using the same names the brief uses, like "AI Service Recommendation").

A dedicated epic for project management

CCSHP-4, Project Planning & Documentation, covers the SRS, WBS, database design, API docs, testing docs, user stories, and use case diagrams the brief asks for — the same documents used for the "Project Management (WBS/Jira Board)" grading criterion.

Screenshots

Taken straight from the live Jira board.

For you

Recent

Starred

Apps

Plans

Spaces

Recent

C Clarke Smart Hire Project

My Software Team

More spaces

Recommended

Collect requests

Filters

Dashboards

Confluence

Teams

Goals

Projects

Customise sidebar

Search

Create

Upgrade

NI

Spaces

C Clarke Smart Hire Project

Summary

Timeline

Backlog

Board

Calendar

List

Forms

Goals

Development

Code

More

Customise your Reports view to suit your space.

126 completed

173 updated

173 created

1 due soon

Status overview

Recent activity

Project summary — 126 of 173 tasks are done, and the activity feed shows recent updates.

For you

Recent

Starred

Apps

Plans

Spaces

Recent

C Clarke Smart Hire Project

My Software Team

More spaces

Recommended

Collect requests

Filters

Dashboards

Confluence

Teams

Goals

Projects

Customise sidebar

Search

Create

Upgrade

NI

Spaces / C Clarke Smart Hire ... / CCSHP-4

Project Planning and Documentation

Description

Child work items

100% Done

Work	Pri...	As...	Status
CCSHP-16 Database Design	M	U	DONE
CCSHP-15 Work Breakdown Structure (WBS)	M	U	DONE
CCSHP-14 User Stories	M	U	DONE
CCSHP-13 Use Case Diagrams	M	U	DONE
CCSHP-12 SRS(Software Requirements Specification)	M	U	DONE
CCSHP-18 API Documentation	M	U	DONE
CCSHP-20 Testing Documentation	M	U	DONE

Email notifications are off until 22/Jul/26

Assignee

Labels

Due date

Team


Start date

Goals


Reporter

Development

Project Planning & Documentation, CCSHP-4 — 100% done, with a clear description and all 7 documents (SRS, WBS, Database Design, API/Testing docs, User Stories, Use Case Diagrams) complete.

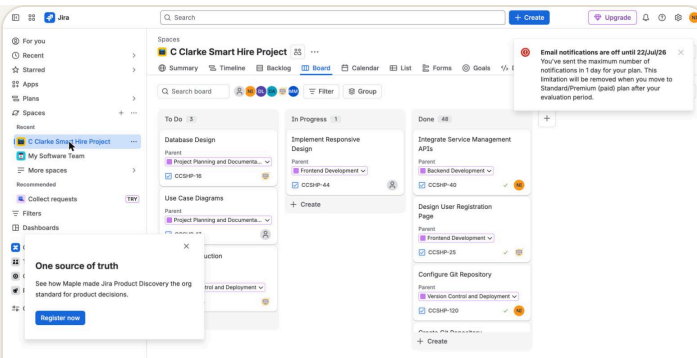

Board view — To Do, In Progress, and Done columns.

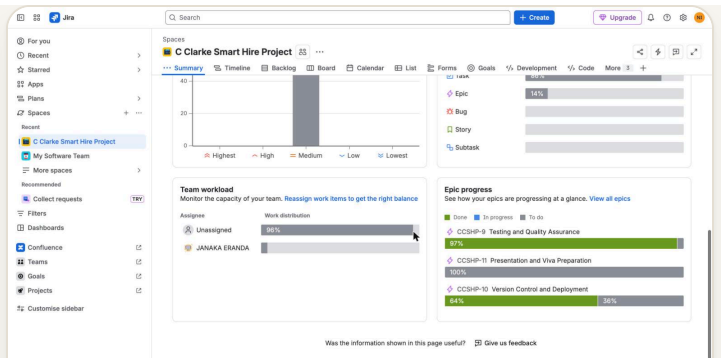

Epic progress — a quick view of how far along each epic is.

Issue List:

Key	Description	Status
GGSHP-174	Zoneless change detection: spinners never resolve after HTTP responses	DONE
GGSHP-175	Table action cells with display:flex break row-height and produce jagged dividers	DONE
GGSHP-176	Admin payments table date column always blank	DONE
GGSHP-177	Navbar notification bell always shows a fake '2 unread' for every user	DONE
GGSHP-178	'Verified provider' badge hardcoded true on every single service card	DONE
GGSHP-179	App fails to boot after merge: OPENAI_API_KEY required env var with no default	DONE
GGSHP-180	500 error on /admin/reviews and /admin/dashboard-stats after merge (missing...	DONE
GGSHP-181	Admin dashboard revenue/bookings chart was 100% hardcoded fake data	DONE

Activity: Add a comment...
 Looks good! Need help? This is blocked... Can you clarify...? 1

Testing & QA epic — the eight bugs below, filed and fixed.

For you

Recent

Starred

Apps

Plans

Spaces

Recent

C Clarke Smart Hire Project

My Software Team

More spaces

Recommended

Collect requests

Filters

Dashboards

Confluence

Teams

Goals

Projects

Customise sidebar

Spaces / C Clarke Smart Hire ... / CCSHP-10

Version Control and Deployment

Description

Edit description

Child work items

64% Done

Work	Pri...	As...	Status
☒ GGSH-120 Configure Git Repository	M	NI	DONE
☒ GGSH-119 Create Git Repository	M	NI	DONE
☒ GGSH-143 Finalize Git Repository	M	NI	DONE
☒ CCSHP-142 Verify Production System	M	U	TO DO
☒ CCSHP-141 Configure Security Settings	M	U	TO DO
☒ CCSHP-140 Fix Deployment Issues	M	U	TO DO
☒ CCSHP-139 Test the Deployed Application	M	U	TO DO
☒ GGSH-138 Run Database Migrations	M	NI	DONE
☒ CCSHP-137 Connect Deployed Frontend and Backend	M	U	TO DO
☒ CCSHP-136 Deploy Frontend Application	M	U	TO DO

Email notifications are off until 22/Jul/26

You've sent the maximum number of notifications in 1 day for your plan. This limitation will be removed when you move to Standard/Premium (paid) plan after your evaluation period.

Assignee

Labels

Due date

Team

Start date

Goals

Reporter

Development

Connect development tools

Open in coding tool

Create branch

Create commit

Version Control & Deployment — git work is done; going live in production is still in progress.

Bugs we found and fixed

These are real bugs we hit while building the app. Each one was logged as a bug report under Testing & QA, with a comment explaining how it was fixed.

CCSHP-174 Zoneless change detection: spinners never resolve after HTTP responses

Several components mutated a plain field inside an `HttpClient.subscribe()` callback. The app has no `zone.js` and never opts into zoneless mode either, so that mutation never triggered a re-render.

Resolved — injected `ChangeDetectorRef` and called `.detectChanges()` in every affected subscribe callback.

CCSHP-175

Table action cells with `display:flex` break row-height and produce jagged dividers

Three tables applied `display: flex` directly to a `<td>`, which breaks the table's row-height layout.

Resolved — moved the flex layout to an inner `<div>` in all three tables.

CCSHP-176 Admin payments table date column always blank

The API response was missing `created_at/updated_at`, so the frontend never received them.

Resolved — added both fields to the schema.

CCSHP-177 Navbar notification bell always shows a fake "2 unread" for every user

The navbar had its own notification code with a fake list built in, used both as the default and when something went wrong.

Resolved — deleted the duplicate logic; navbar now uses the existing, correct notification store.

CCSHP-178 "Verified provider" badge hardcoded true on every single service card

The API response never had a verification field at all — the frontend just always rendered the static text, despite a full admin verification workflow already existing.

Resolved — added `provider_verified` to the service response, wired through the frontend.

CCSHP-179

App fails to boot after merge: OPENAI_API_KEY required env var with no default

A teammate's merge made a previously-optional setting required with no default, crashing the backend for anyone without the key configured.

Resolved — reverted to optional; the AI service already guarded for a missing key.

CCSHP-180

500 error on /admin/reviews and /admin/dashboard-stats after merge (missing DB column)

A new column was added to the code, but not to the live database. This project doesn't use database migrations — it only creates new tables automatically, it doesn't update existing ones.

Resolved — added the column directly in the live database and backfilled existing rows.

CCSHP-181 **Admin dashboard revenue/bookings chart was 100% hardcoded fake data**

The chart rendered invented numbers with no relationship to real bookings or payments.

Resolved — added a real revenue-timeseries endpoint and wired the chart to it.

Who worked on what

The five people below are the whole team. Tasks were assigned based on who actually did that part of the work.

Nilan Iddawela Backend APIs, admin, AI features, messaging, QA, git workflow, documentation 32 commits	Janaka Eranda Login & account status, database schema, profile/dashboard pages 37 commits	Dasun Anjana Bookings, notifications, availability (frontend & backend) 28 commits
Damith Lasantha AI feature backend & recommendation logic 5 commits	Matheesha Milan Landing page, services/categories/search backend 4 commits, reporter	

What's still open: Presentation & Viva Prep is 0% because that work happens closer to the viva date. A few Version Control tasks are still open too — deploying to production, setting up the production database, and security config — since the app currently runs locally.

This covers all 8 epics on the CCSHP board. Full detail on every task is in the board's own activity history on Jira.
